

nDARS Project

ID	Task Name	Predicted Hrs	Duration	Start	Finish	Predecessor	Resource Names	2005				
								Oct	Jan	Apr	Jul	
1	Degree Audit Replacement System		600 days?	Mon 1/3/05	Tue 4/17/07							
2	System Planning and Design - changesto support undergraduate students in College, Arts and Arch, TF&T entering =>08Fall		600 days?	Mon 1/3/05	Tue 4/17/07		CIS,AIS (SR,Admissions,DT)					
3	Review survey and follow-up responses	120	86 days	Mon 1/3/05	Mon 5/2/05		CIS					
4	Articulation data: stored in SR and displayed via Transfer Credit Detail and Summary (TRCD/ TRCR) screens for ugs (College,TFT,A&A) entering term >= 08Fall	24	348 days?	Tue 12/20/05	Tue 4/17/07	3	CIS[50%],AIS John C[50%]					
5	specs for modifications to TRCD and TRCR screens in support of multiple systems (including grade calc/re-calc)	24	10 days	Tue 12/20/05	Mon 1/2/06	3	AIS John C[75%],CIS[25%]					
6	1/3/07 need to write spec, do after Proficiency spec and CAR analysis is done		42 days?	Mon 2/19/07	Tue 4/17/07	31						
7	1/3/07 need data mapping, use of data within screens and SR0 and business logic (TRCD then TRCR): do after CAR		1 day?	Mon 2/19/07	Mon 2/19/07	31						
8	1/24/07 check for SR2 specs or documentation for these screens		6 days	Wed 1/24/07	Wed 1/31/07		Arun					
9	Mods to single and batch DPR requests specifications: SR0 PROG and ORDR screens, Counselor Desktop, URSA	24	444.25 days?	Tue 5/3/05	Wed 1/10/07	3	AIS John C,AIS DT PGR					
10	1/3/07 have spec		42 days?	Thu 10/20/05	Fri 12/16/05							
11	1/3/07 review and update spec		0.25 days?	Tue 5/3/05	Tue 5/3/05		CIS,RO,UARS,AIS					
12	group review: ready to go and actionable?		0.25 days?	Wed 1/10/07	Wed 1/10/07	11	CIS,RO,UARS,AIS					
13	Exemption and Substitution Processing specifications: for ugs (College,TFT,A&A) entering term >= 08Fall store data only in nDARS, <08Fall, only in SR0 DAUD	24	444.25 days?	Tue 5/3/05	Wed 1/10/07	3	AIS John C[5%],CIS[95%]					
14	1/3/07 have spec		1 day?	Sun 4/23/06	Sun 4/23/06							
15	1/3/07 review and update spec		0.25 days?	Tue 5/3/05	Tue 5/3/05		CIS,RO,UARS,AIS					
16	group review: done?		0.25 days?	Wed 1/10/07	Wed 1/10/07	15	CIS,RO,UARS,AIS					
17	System Access specifications	24	502 days?	Tue 5/3/05	Fri 3/30/07	3	AIS John C[5%],CIS[95%]					
18	1/3/07 have spec		34 days?	Tue 11/1/05	Fri 12/16/05							
19	1/3/07 review and update spec		0.25 days?	Tue 5/3/05	Tue 5/3/05		CIS,RO,UARS,AIS					
20	group review: done?		58 days?	Wed 1/10/07	Fri 3/30/07	19	CIS,RO,UARS,AIS					
21	Security specifications	8	444.25 days?	Tue 5/3/05	Wed 1/10/07	3	AIS John C[5%],CIS[95%]					
22	1/3/07 have spec		136 days?	Sun 6/12/05	Fri 12/16/05							
23	1/3/07 review and update spec		0.25 days?	Tue 5/3/05	Tue 5/3/05		CIS,RO,UARS,AIS					

nDARSSchedule20070214
Date: Tue 3/13/07

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

nDARS Project

ID	Task Name	Predicted Hrs	Duration	Start	Finish	Predecess	Resource Names	2005			
								Oct	Jan	Apr	Jul
24	group review: done?		0.25 days?	Wed 1/10/07	Wed 1/10/07	23	CIS,RO,UARS,AIS				
25	Advanced Placement (AP) Test Scores Processing specifications	24	419 days?	Thu 8/25/05	Fri 3/30/07	3	UARS[50%],CIS[50%]				
26	1/3/07 have spec		324 days?	Thu 8/25/05	Fri 11/17/06						
27	1/3 /07 review spec: what's missing?		21 days?	Wed 1/3/07	Wed 1/31/07		CIS,RO,UARS,AIS				
28	1/3/07 need to define record layout for data to be sent from UA0 to nDARS (replace UARS feed to my.ucla)		1 day?	Wed 1/3/07	Wed 1/3/07		AIS John C[50%],CIS[50%]				
29	1/31/07 another option is for SR0#D888 to create file for CIS -- see meeting notes		1 day?	Wed 1/31/07	Wed 1/31/07						
30	group review: done?		58 days?	Wed 1/10/07	Fri 3/30/07		CIS,RO,UARS,AIS				
31	Proficiency Data Element Processing specifications	88	389 days?	Thu 8/25/05	Fri 2/16/07	3	AIS John C[5%],CIS[90%],AIS - Admissions PGR[5%]				
32	SR0 College Academic Requirements (by student) (CAR) - screens, data and processing		389 days?	Thu 8/25/05	Fri 2/16/07						
33	1/3/07 have spec		82 days?	Thu 8/25/05	Fri 12/16/05						
34	1/3/07 review and update spec from perspective of COM processing		1 day?	Wed 1/3/07	Wed 1/3/07		Praveen Dugar				
35	1/3/07 need data mapping, use of data within screen and SR0 and business logic	60	21 days?	Wed 1/3/07	Wed 1/31/07		Marietta Nieto				
36	group review: ready to go and actionable?		28 days	Wed 1/10/07	Fri 2/16/07		CIS,RO,UARS,AIS				
37	1/10/07CAR analysis right on track with some revision to format and content: will continue. OK to start testing COM (nDARS to SR0) and meet 1/17 to review		1 day	Wed 1/10/07	Wed 1/10/07						
38	1/17/07 continued review with corrections and further actions		1 day	Wed 1/17/07	Wed 1/17/07						
39	1/24/07 ditto - see meeting notes		1 day	Wed 1/24/07	Wed 1/24/07		AIS,CIS,RO,UARS				
40	1/31/07 reviewed UA0-SRS Interface (SR0#D888) - see meeting notes		1 day	Wed 1/31/07	Wed 1/31/07		CIS,AIS,RO,UARS				
41	2/7/07 continued UA0-SRS Interface (SR0#D888) - see meeting notes		1 day	Wed 2/7/07	Wed 2/7/07		CIS,AIS,RO,UARS				
42	2/14/07 repeat processing, sequence restrictions: will have courses with term taken in nDARS, by admit term in SR		1 day	Wed 2/14/07	Wed 2/14/07		CIS,AIS,RO,UARS				
43	2/16/07 finish UA0-SRS Interface (SR0#D888)		1 day	Fri 2/16/07	Fri 2/16/07		CIS,AIS,RO,UARS				
44	2/21/07 RK212 - English/Subject A/ESL		1 day	Fri 2/16/07	Fri 2/16/07		CIS,AIS,RO,UARS				
45	specs for coordinating dictionary changes	24	53 days	Wed 1/17/07	Fri 3/30/07	3	AIS John C,CIS				
46	1/17/07 RO needs to notify CIS when data elements used by nDARS are changed ie., new values: 1/24/07 RO will add Robert Kilgore to email list		6 days	Wed 1/17/07	Wed 1/24/07		Arun				

nDARSSchedule20070214
Date: Tue 3/13/07

Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

nDARS Project


ID	Task Name	Predicted Hrs	Duration	Start	Finish	Predecess	Resource Names	2005			
								Oct	Jan	Apr	Jul
47	1/24/07 agreed to leave existing data values 'as is'		6 days	Wed 1/17/07	Tue 1/30/07		AIS,CIS,RO,UARS				
48	1/24/07 anything more needed here or can this be marked complete?		48 days	Wed 1/24/07	Fri 3/30/07		AIS				
49	specs for coordinating a Requirements Table of Record	96	5 days?	Wed 1/24/07	Tue 1/30/07	3	AIS,College,RO				
50	1/3/07 anything needed here or can this be marked complete?		5 days?	Wed 1/24/07	Tue 1/30/07		AIS,CIS,RO,UARS				
51	specs for modifications to any other SR0: tables, screens, processing	96	63 days?	Wed 1/3/07	Fri 3/30/07	3	AIS John C[50%],CIS[50%]				
52	1/3/07 anything needed here or can this be marked complete?		63 days?	Wed 1/3/07	Fri 3/30/07		AIS				
53	1/3/07 Exemptions and Substitutions: SR0/DAUD will only have records for students entering < 08Fall - do we need to add screen edit?		63 days?	Wed 1/3/07	Fri 3/30/07		CIS,RO,UARS,AIS				
54	specs for synchronization, backup and recovery between SR, and both new and legacy system	96	25 days?	Wed 1/3/07	Tue 2/6/07	3	AIS John C[50%],CIS[50%]				
55	1/3/07 anything needed here or can this be marked complete?		20 days?	Wed 1/3/07	Tue 1/30/07		AIS				
56	1/17/07 system seems to self-correct when audits are performed as long as nDARS always respects SR0 satisfied values (Bonnie send diagram to Deborah)		6 days	Wed 1/17/07	Wed 1/24/07		AIS,CIS,RO,UARS				
57	synchronization built into test score processing - batch (SR0D888) and online (TRCD)		1 day?	Tue 2/6/07	Tue 2/6/07		AIS,CIS,RO,UARS				
58	XML Schema specifications - not phase 1: will develop when UCLA needs it	96	418 days?	Tue 5/3/05	Mon 12/4/06	3	CIS				
59	1/3/07 have spec: not needed this phase		308 days?	Mon 10/3/05	Mon 12/4/06						
60	1/3 /07 review spec		0.25 days?	Tue 5/3/05	Tue 5/3/05		CIS,RO,UARS,AIS				
61	done?		0.25 days?	Tue 5/3/05	Tue 5/3/05		CIS,RO,UARS,AIS				
62	Printing specifications	24	400 days?	Mon 8/22/05	Wed 2/28/07	3	CIS				
63	1/3/07 have spec		49 days	Mon 8/22/05	Thu 10/27/05		CIS				
64	1/3/07 review and update spec		20.5 days?	Wed 1/31/07	Wed 2/28/07		CIS,RO,UARS,AIS				
65	group review: ready to go and actionable?		1 day?	Wed 1/10/07	Wed 1/10/07		CIS,RO,UARS,AIS				
66	System Input specifications	24	444.25 days?	Tue 5/3/05	Wed 1/10/07	3	RO[20%],CIS[80%]				
67	1/3/07 have spec		1 day	Mon 8/15/05	Mon 8/15/05						
68	1/3/07 review and update spec		0.25 days?	Tue 5/3/05	Tue 5/3/05		CIS,RO,UARS,AIS				
69	group review: done?		0.25 days?	Wed 1/10/07	Wed 1/10/07	68	CIS,RO,UARS,AIS				

nDARSSchedule20070214
Date: Tue 3/13/07

Task  Progress  Summary  External Tasks  Deadline 
 Split  Milestone  Project Summary  External Milestone 

nDARS Project

ID	Task Name	Predicted Hrs	Duration	Start	Finish	Predecessor	Resource Names	2005			
								Oct	Jan	Apr	Jul
70	Source Editor specifications	240	444.25 days?	Tue 5/3/05	Wed 1/10/07	3	UARS David Darling[10%],UARS Daniel				
71	1/3/07 have spec		1 day	Thu 3/30/06	Thu 3/30/06						
72	1/3/07 review and update spec		0.25 days?	Tue 5/3/05	Tue 5/3/05		CIS,RO,UARS,AIS				
73	group review: done?		0.25 days?	Wed 1/10/07	Wed 1/10/07	72	CIS,RO,UARS,AIS				
74	Department Planner specifications - 1/10/07 not this phase?	0	0 days	Mon 5/2/05	Mon 5/2/05	3					
75	Report Scheduler specifications	24	530.25 days?	Mon 1/3/05	Wed 1/10/07						
76	1/3/07 have spec		1 day	Sat 4/15/06	Sat 4/15/06						
77	1/3/07 review and update spec		0.25 days?	Mon 1/3/05	Mon 1/3/05		CIS,RO,UARS,AIS				
78	group review: done?		0.25 days?	Wed 1/10/07	Wed 1/10/07	77	CIS,RO,UARS,AIS				
79	Detail Design and Construction		731 days?	Mon 1/3/05	Wed 10/17/07						
80	Audit Input Component Development	40	14 days	Wed 1/10/07	Tue 1/30/07	66	RO[80%],CIS[20%]				
81	TRCD & TRCR Component Development	240	130 days	Wed 4/18/07	Tue 10/16/07	4,5	RO[25%],AIS John C[25%],CIS[50%]				
82	AP Test Scores/Placement Exam Processing Component Development	160	93.87 days	Mon 4/2/07	Thu 8/9/07	25	CIS[75%],UARS[25%]				
83	Proficiency Data Element Processing	88	545 days?	Mon 1/3/05	Tue 1/30/07		AIS John C[5%],CIS[90%],AIS - Admissions PGR[5%]				
84	Develop COM		170 days?	Thu 5/25/06	Wed 1/17/07		Praveen Dugar				
85	Develop Web Service		170 days?	Thu 5/25/06	Wed 1/17/07		Praveen Dugar				
86	Unit test COM and Web Service		163 days?	Mon 6/5/06	Wed 1/17/07		Praveen Dugar;John Cramer				
87	Client Web applications development		3 days?	Thu 6/15/06	Mon 6/19/06		Chris Spritzer				
88	Client testing -- 1/24/07 will start when Chris is back		20 days	Wed 1/3/07	Tue 1/30/07		Chris Spritzer,Praveen Dugar,RO				
89	Sign-off		1 day?	Mon 1/3/05	Mon 1/3/05		Stakeholders				
90	Subs/Exempts Component Development	120	45 days	Wed 1/10/07	Wed 3/14/07	13	CIS				
91	Department Planner Component Development	0	0 days	Mon 5/2/05	Mon 5/2/05	74					
92	Web Service Component Development	200	48 days	Tue 12/5/06	Thu 2/8/07	58	CIS				

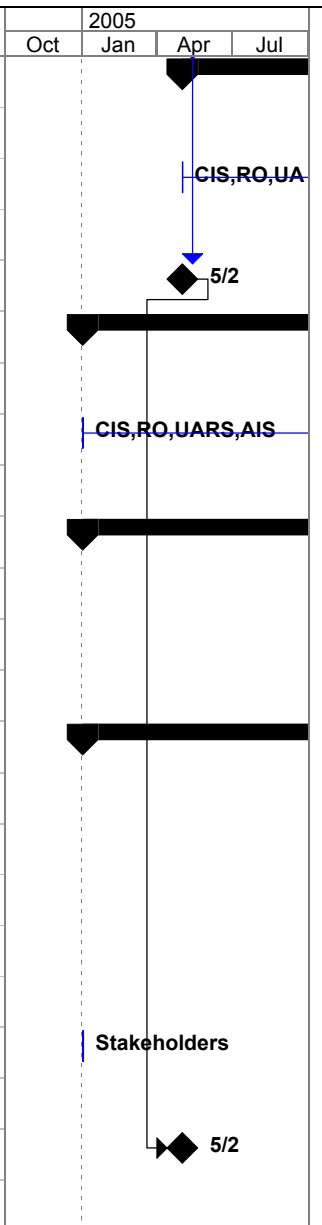






nDARSSchedule20070214
Date: Tue 3/13/07




Task		Progress		Summary		External Tasks		Deadline	
Split		Milestone		Project Summary		External Milestone			

nDARS Project

ID	Task Name	Predicted Hrs	Duration	Start	Finish	Predecessor	Resource Names	2005			
								Oct	Jan	Apr	Jul
93	Generic Audit Report (example of using XML schema)	160	45 days	Fri 2/9/07	Thu 4/12/07	92	CIS				
94	Modify Existing Audit Service	80	66 days	Fri 12/29/06	Fri 3/30/07		AIS Pgm				
95	Encode Articulation Rules (1)	540	110 days	Mon 5/2/05	Thu 9/29/05		UARS Rosanna[70%],UARS1[70%],UAR				
96	Source Editor Component Development	480	120 days	Wed 1/10/07	Wed 6/27/07	70	CIS				
97	Print Service Component Development	320	130 days	Thu 3/1/07	Wed 8/29/07	62	CIS				
98	Major Requirement Encoding		369 days	Thu 1/5/06	Fri 6/1/07		CIS				
99	College Requirements	860	369 days	Thu 1/5/06	Fri 6/1/07		CIS				
100	School of Theater, Film & Television Requirements	200	65 days	Fri 12/1/06	Thu 3/1/07		CIS				
101	School of Arts & Architecture Requirements	200	65 days	Fri 12/1/06	Thu 3/1/07		CIS				
102	Encode Articulation Rules (2)	540	108 days	Mon 5/1/06	Wed 9/27/06		UARS Rosanna[70%],UARS1[70%],UAR				
103	Test Readiness Review of TCA/credit components	120	108 days	Mon 5/1/06	Wed 9/27/06		CIS				
104	Signoff and implementation for UARS - Phase 1 (TCA/creditcomponents fully auditable against reqs)	4	1 day	Wed 10/17/07	Wed 10/17/07	96,81,90	UARS David Darling[10%],UARS Daniel Fogg[20%],UARS				
105	Train staff (evaluation and processing staff) on new system - Enter Fall '06 Source Data for test and compariosn	80	44 days	Tue 8/1/06	Fri 9/29/06		UARS Daniel Fogg[20%],UARS Rosanna[20%],UARS				
106	Enter Fall '07 Source Data	540	131 days	Thu 3/29/07	Thu 9/27/07		UARS				
107	Test and Configuration	240	130 days	Thu 9/28/06	Wed 3/28/07	103	CIS				
108	Train Staff for System Use	120	152 days	Wed 11/1/06	Thu 5/31/07		CIS				
109	DARS Ready for Production Use- Phase 2	0	0 days	Mon 4/2/07	Mon 4/2/07	107					

nDARSSchedule20070214
Date: Tue 3/13/07

Task  Progress  Summary  External Tasks  Deadline 

Split  Milestone  Project Summary  External Milestone 
